

Ref No.: BD-ACEPM-SAMCO-LET-037

Date: Sunday, 17th of May 2026

To: SAMCO National Construction Company
Attention: Eng. Mohammed Sami Mohammed (Project Manager)

Project Name: The Big Business District
Contract/Package: Construction Works of the Civil Works for Buildings B1, B2, B3 and B4

Subject: Notice of Slow Progress Rate and Comments on Monthly Progress Report – April 2026

Reference (S):

- 1) The Contractor's monthly report, submitted via email on 30-April-2026.

Dear Sir,

With reference to the above-mentioned subject and the Contractual obligations stipulated in the signed Contract and the Monthly Report Ref. no. 1, the Engineer formally expresses its concern regarding the Contractor's inability to maintain the required progress in executing critical Project activities, as set forth in the approved Programme.

It has become apparent that the Contractor has not met the performance expectations outlined in the Programme, as evidenced by the latest project performance evaluation and the following key performance indicator:

$$SPI = EV / PV = 29.38 / 62 = 0.47.$$

These indicators clearly reflect the ongoing delay in executing the Project activities, causing a significant deviation from the approved Programme. This deficiency is impeding the overall progress of the Works and poses a serious risk of further slippage in the Contractual Time for Completion.

On the other hand, Attachment No. (01) includes all comments related to the previously submitted Monthly Report for April 2026. Accordingly, the Contractor is hereby requested to address the mentioned comments, amend the report accordingly, and to submit the report officially for further necessary action as the report has not been submitted through official channels.

In light of the above, and in accordance to Sub Clauses 3.3[Instructions of the Engineer], 8.3 [Programme] and 8.6 [Rate of Progress] of the contract, the Contractor is requested to exert its utmost endeavors to recover the accrued delay by taking immediate corrective action to improve its performance through the proper allocation of resources, avoid any negative impact on the overall project timeline, and provide a detailed report outlining the mitigation measures adopted to expedite project progress and effectively address these delays.



AS
M.S

ACE Project Management | ACE Group
12 Makram Ebied st. -Nasr City - Cairo
Nasr City, Cairo, Egypt
Tel : + 202 2273 8566
Tel : + 202 7385 4677
E-mail: ace.ho@ace-mb.com



The Engineer hereby notifies the Contractor that it shall be held liable for consequences resulting from non-compliance with the above.

Yours faithfully,
Eng. Abdelaziz Mohammed
Project Manager,
ACE Project Management

A blue rectangular stamp with a double border. Inside, the text "ACE-PM" is at the top, "MOHARRAM BAKHOUM" is in the middle, and "THE BIG" is at the bottom. A signature is written over the stamp.

Attachment(s):

1. Comments on Monthly Report April 2026

CC:

Eng. Mohamed Hamza - Projects Manager
Eng. Mostafa Gala - Owner representative
Eng. Ahmed Saafan – Project Controls Director
Eng. Ramy Refaat – Commercial Contracts Director
Eng. Osama Waly – PCO representative

ACE-PM Monthly Review Report – APR.2026


- General:**

- The cut-off date of the current report shall be **25-Apr-2026**.

- Based on the submitted monthly report:

Updated Date	15-April-2026
--------------	---------------

- Based on the submitted XER file:

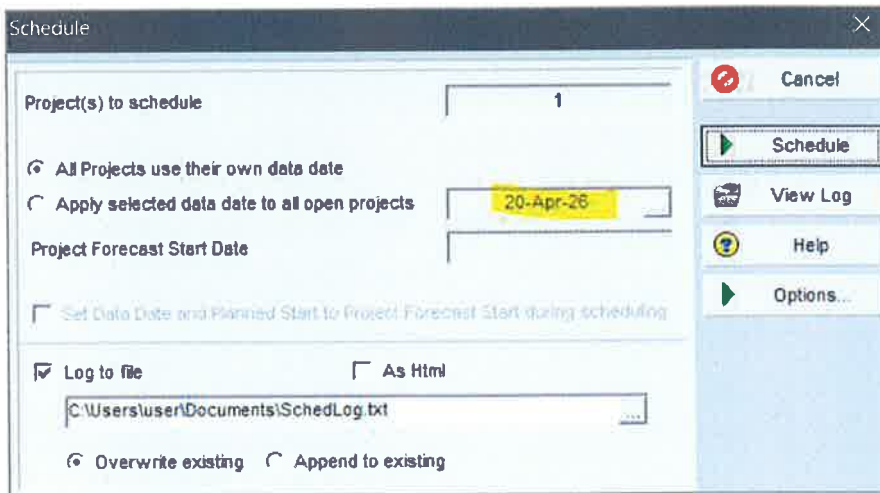

- On page 7, under “Progress Status for Each Building”:

Conclusion:

- Building 1 is behind schedule by 118 days delay
- Building 2 is behind schedule by 102 days delay
- Building 3 is behind schedule by 102 days delay
- Building 4 is behind schedule by 103 days delay

- Based on the submitted XER file:

Handover Works		52	0%	15-Jun-27	05-Aug-27	0%	06-Mar-27	10-Apr-27	-117
HO-1020	Snag list for B02	10	0% <td>15-Jun-27</td> <td>24-Jun-27</td> <td>0%<td>06-Mar-27</td><td>20-Mar-27</td><td>-66</td></td>	15-Jun-27	24-Jun-27	0% <td>06-Mar-27</td> <td>20-Mar-27</td> <td>-66</td>	06-Mar-27	20-Mar-27	-66
HO-1030	Snag list for B03	10	0% <td>26-Jun-27</td> <td>06-Jul-27</td> <td>0%<td>14-Mar-27</td><td>24-Mar-27</td><td>-77</td></td>	26-Jun-27	06-Jul-27	0% <td>14-Mar-27</td> <td>24-Mar-27</td> <td>-77</td>	14-Mar-27	24-Mar-27	-77
HO-1010	Snag list for B01	10	0% <td>24-Jul-27</td> <td>03-Aug-27</td> <td>0%<td>28-Mar-27</td><td>07-Apr-27</td><td>-101</td></td>	24-Jul-27	03-Aug-27	0% <td>28-Mar-27</td> <td>07-Apr-27</td> <td>-101</td>	28-Mar-27	07-Apr-27	-101
HO-1040	Snag list for B04	10	0% <td>08-Jul-27</td> <td>19-Jul-27</td> <td>0%<td>28-Mar-27</td><td>07-Apr-27</td><td>-88</td></td>	08-Jul-27	19-Jul-27	0% <td>28-Mar-27</td> <td>07-Apr-27</td> <td>-88</td>	28-Mar-27	07-Apr-27	-88
HO-1050	Snag list for As-Built	2	0% <td>28-Jul-27</td> <td>30-Jul-27</td> <td>0%<td>06-Apr-27</td><td>07-Apr-27</td><td>-114</td></td>	28-Jul-27	30-Jul-27	0% <td>06-Apr-27</td> <td>07-Apr-27</td> <td>-114</td>	06-Apr-27	07-Apr-27	-114
HO-1000	Demobilization	2	0% <td>04-Aug-27</td> <td>05-Aug-27</td> <td>0%<td>08-Apr-27</td><td>10-Apr-27</td><td>-101</td></td>	04-Aug-27	05-Aug-27	0% <td>08-Apr-27</td> <td>10-Apr-27</td> <td>-101</td>	08-Apr-27	10-Apr-27	-101

- On page 8, under “Activity Key Achievement”:

Reinforced Concrete (RC Raft) - Reinforcement	B01	Completion of Reinforcement (RFT) and Concrete Pouring.	100% Completed
	B02	Completion of Reinforcement (RFT) and Concrete Pouring.	100% Completed
	B03	Completion of Reinforcement (RFT) and Concrete Pouring.	100% Completed
	B04	Reinforcement (RFT) and Concrete Pouring In Progress.	30% Completed

- Based on the submitted XER file:

CON-B04-FOOT-1080	Pouring for RC Raft & Footings (B04) (footing)	2	50%	12-Mar-25 A	25-Apr-26
-------------------	--	---	-----	-------------	-----------

- The Contractor shall verify the reported progress percentages in line with the actual site status.

- **Scheduling:**

- Activities without successors:

CON-B02-FOOT-1080	Pouring Columns & Walls Below SOG (B01) (footing)
P-MDEL-1060	Delivery for cold Crystalline waterproofing for Water tank

- Out-of-sequence activities:

CON-B01-FOOT-1050	RFT for RC Raft & Footings (B01) (footing)
CON-B01-FOOT-1070	RFT for Columns & Walls Below SOG (B01) (footing)
CON-B02-FOOT-1050	RFT for RC Raft & Footings (B02) (footing)
CON-B02-FOOT-1070	RFT for Columns & Walls Below SOG (B02) (footing)
CON-B03-BAS02-1000	Scaffolding works for Walls, Col. & Cores (B03) (Bas 02)
CON-B03-BAS02-1010	RFT for Walls, Col. & Cores (B03) (Bas 02)
CON-B03-BAS02-1020	Shuttering for Walls, Col. & Cores (B03) (Bas 02)
CON-B03-BAS02-1030	Pouring for Walls, Col. & Cores (B03) (Bas 02)
CON-B03-FOOT-1050	RFT for RC Raft & Footings (B03) (footing)
CON-B03-FOOT-1070	RFT for Columns & Walls Below SOG (B03) (footing)
CON-B04-FOOT-1050	RFT for RC Raft & Footings (B04) (footing)
CON-B04-FOOT-1070	RFT for Columns & Walls Below SOG (B04) (footing)
CON-B04-FOOT-1080	Pouring for RC Raft & Footings (B04) (footing)
CON-B04-WT-1070	RFT for RC Raft (B04) (Water Tank)
CON-B04-WT-1110	RFT for Walls (B04) (Water Tank)
CON-B04-WT-1130	Pouring for Walls (B04) (Water Tank)

- The Contractor shall resolve all out-of-sequence activities in the upcoming updates and submit a change report.

- The number of critical activities is 573 out of 1,363 (42%), which indicates an increased level of project risk.

- **Conclusion:**

- The Contractor shall do his utmost to mitigate the project delays.
